Roof Report

Prepared by Rich Roofing & Services LLC

3879 sqft

13 facets

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

Predominant pitch 6/12


Bruce Cron



This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Diagram

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

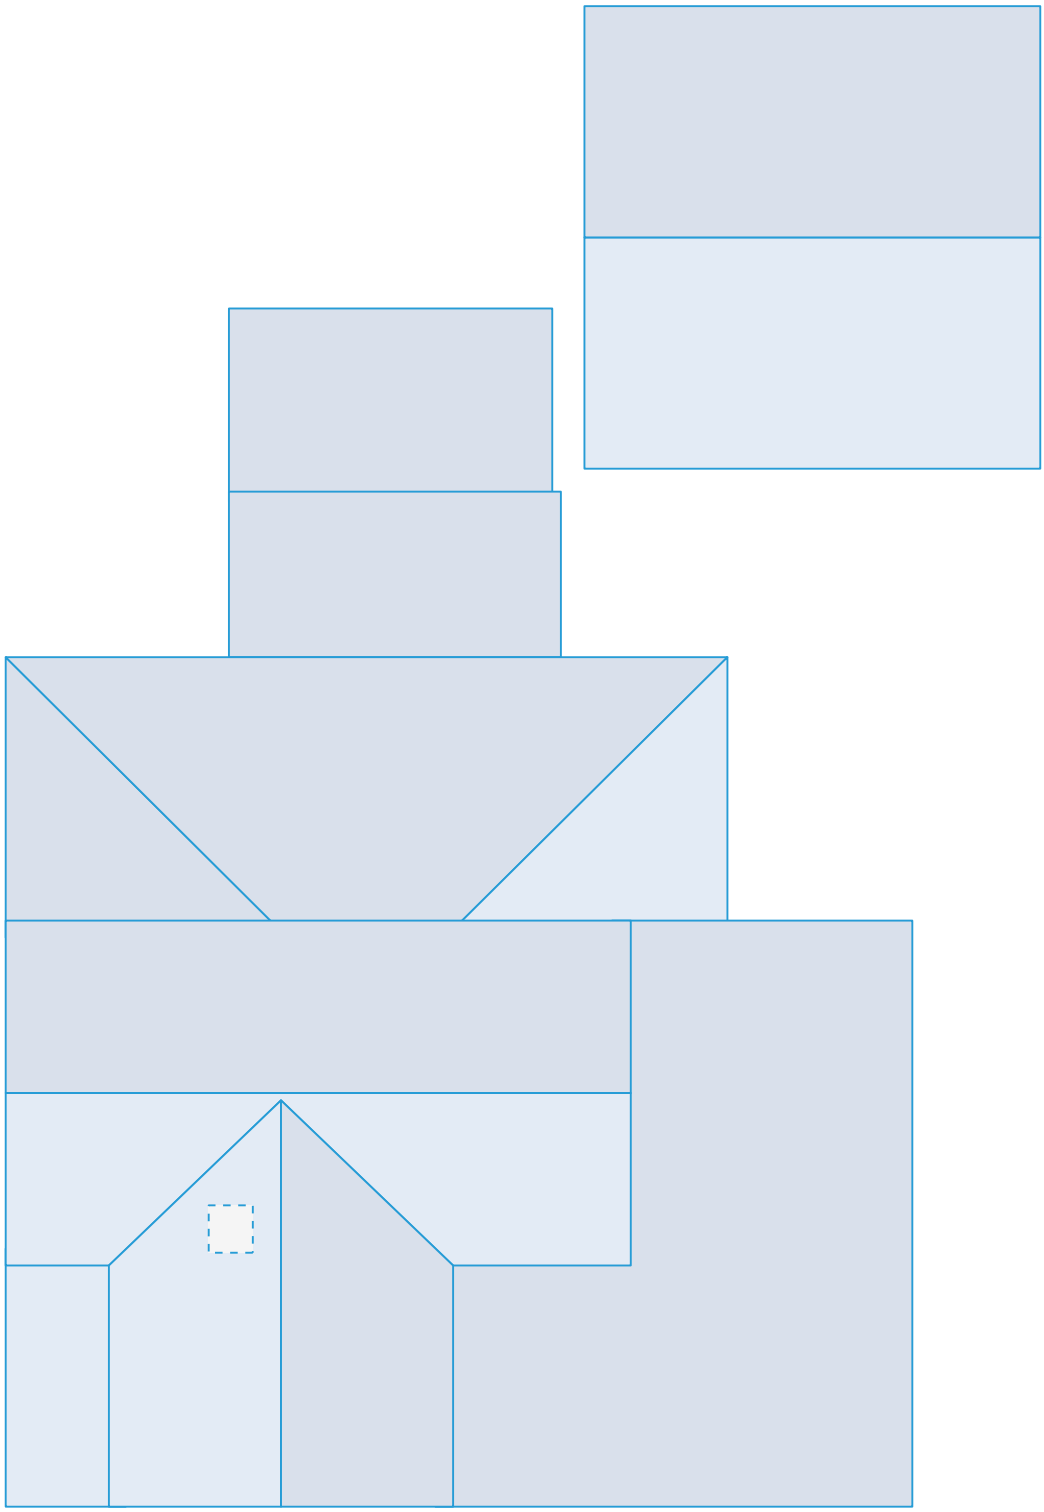


This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Length measurement report

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

- Eaves: 269ft 8in
- Ridges: 87ft 6in
- Step flashing: 56ft 8in
- Unspecified: 0ft 0in
- Valleys: 30ft 0in
- Rakes: 226ft 3in
- Transitions: 18ft 10in
- Hips: 47ft 11in
- Wall flashing: 77ft 6in
- Parapet wall: 0ft 0in

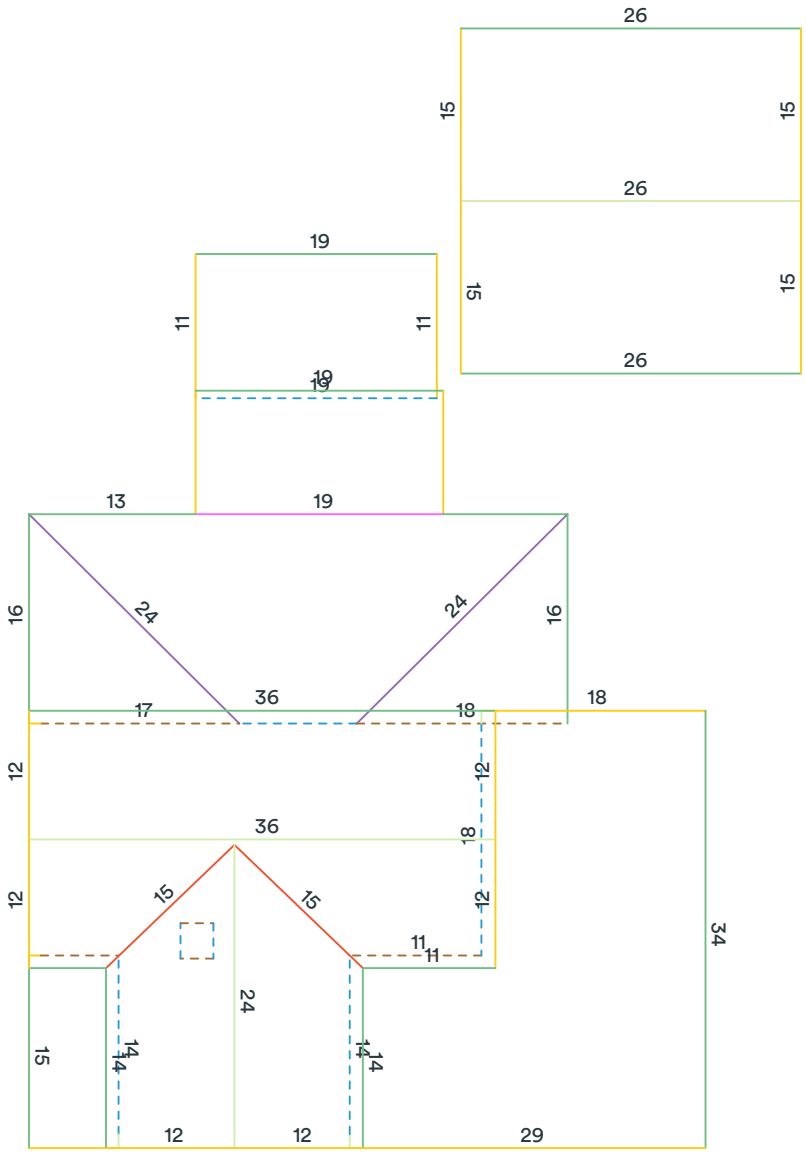

Measurements in diagram are rounded up for display. Some edge lengths may be hidden from diagram to avoid overcrowding.


This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Area measurement report

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

Total roof area: 3879 sqft
Pitched roof area: 3677 sqft
Flat roof area: 202 sqft
Two story area: 0 sqft
Two layer area: 0 sqft

Predominant pitch: 6/12
Predominant pitch area: 1489 sqft
Unspecified pitch area: 0 sqft

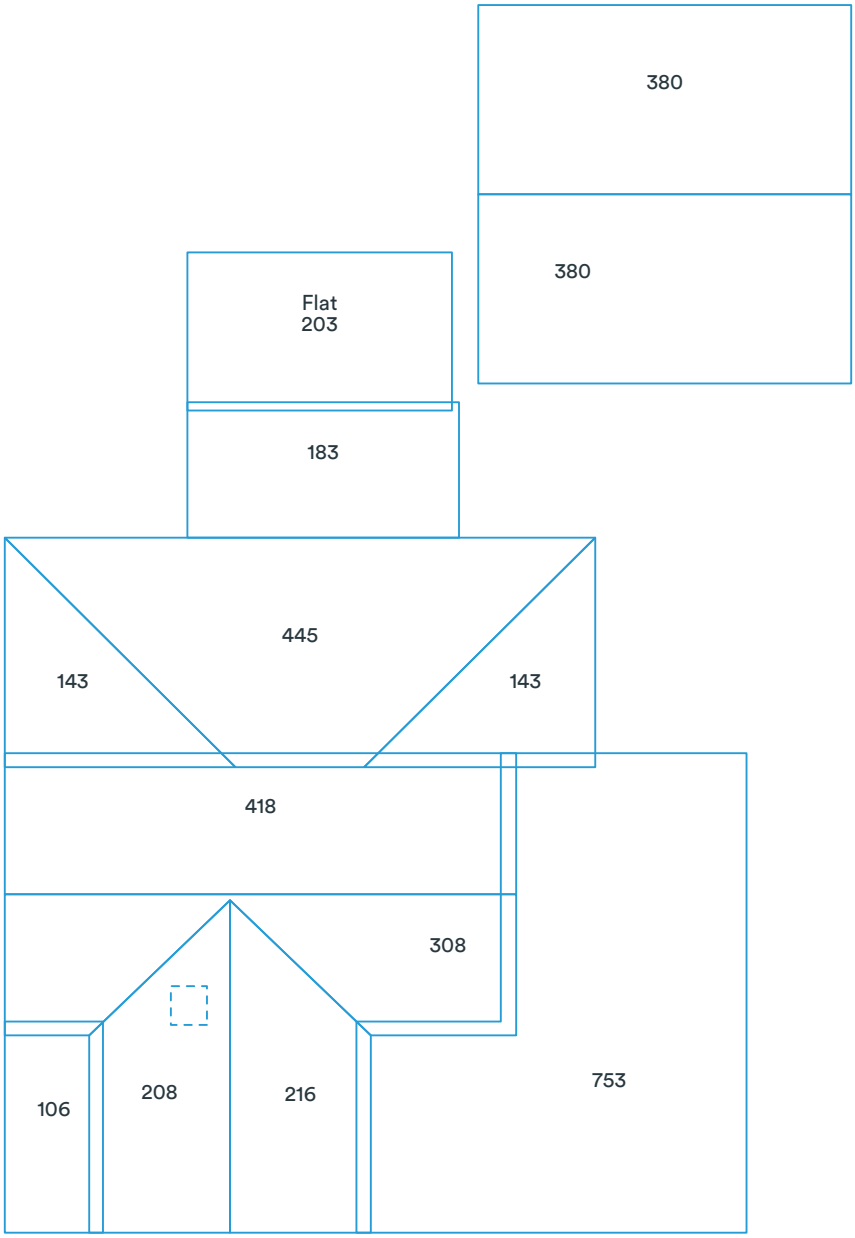


Area measurements in diagram are rounded. The totals at the top of the page are the sums of the exact measurements, which are then rounded. Deleted facets (skylights, chimneys, etc.) are designated with a dashed line and are excluded from the calculations.

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Pitch & direction measurement report

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

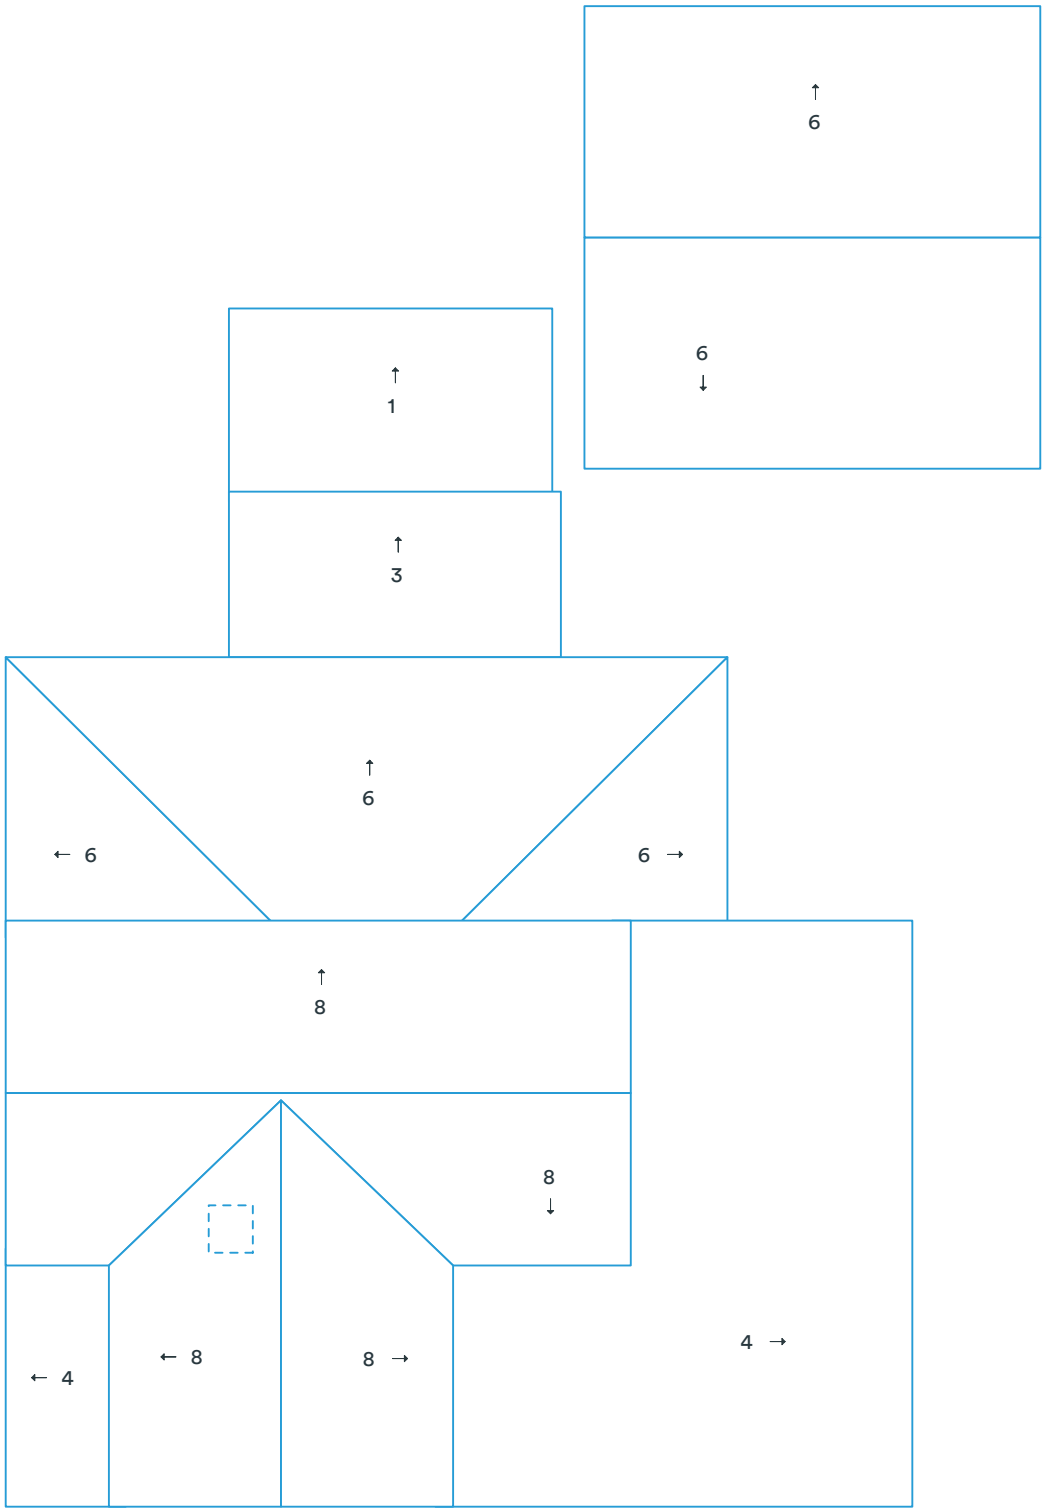


Deleted facets are designated with a dashed line and do not have a pitch.

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Structure #1 summary

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

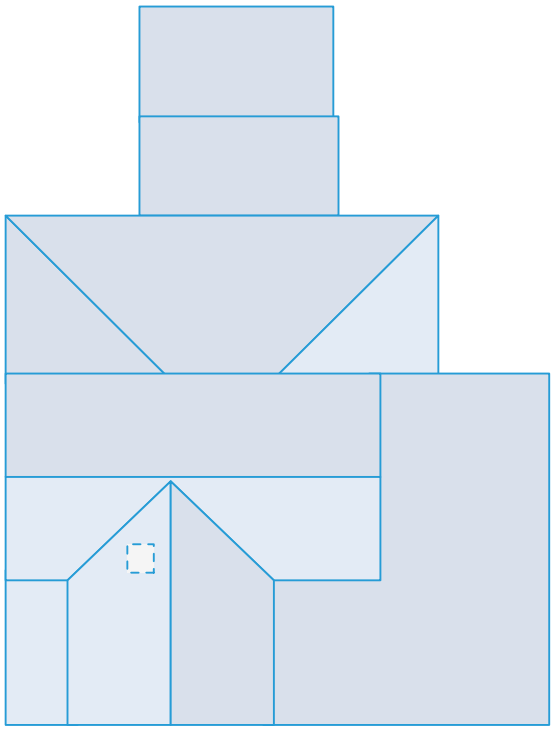

Measurements

Total roof area	3120 sqft
Total pitched area	2918 sqft
Total flat area	202 sqft
Total roof facets	11 facets
Predominant pitch	8/12
Total eaves	217ft 11in
Total valleys	30ft 0in
Total hips	47ft 11in
Total ridges	61ft 7in
Total rakes	167ft 6in
Total wall flashing	77ft 6in
Total step flashing	56ft 8in
Total transitions	18ft 10in
Total parapet wall	0ft 0in
Total unspecified	0ft 0in
Hips + ridges	109ft 6in
Eaves + rakes	385ft 5in

Pitch	1/12	3/12	4/12	6/12	8/12
Area (sqft)	203	183	858	730	1,149
Squares	2.1	1.9	8.6	7.3	11.5


			Recommended				
Waste %	0%	10%	12%	15%	17%	20%	22%
Area (sqft)	3,120	3,432	3,495	3,588	3,651	3,744	3,807
Squares	31.2	34.4	35.0	35.9	36.6	37.5	38.1

Recommended waste is based on an asphalt shingle roof with a closed valley system (if applicable). Several other factors are involved in determining which waste percentage to use, including the complexity of the roof and individual roof application style. You will also need to calculate the post-waste quantity of other materials needed (hip and ridge caps, starter shingle, etc.).

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Structure #2 summary

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326



Measurements

Total roof area	760 sqft
Total pitched area	760 sqft
Total flat area	0 sqft
Total roof facets	2 facets
Predominant pitch	6/12
Total eaves	51ft 9in
Total valleys	0ft 0in
Total hips	0ft 0in
Total ridges	25ft 11in
Total rakes	58ft 9in
Total wall flashing	0ft 0in
Total step flashing	0ft 0in
Total transitions	0ft 0in
Total parapet wall	0ft 0in
Total unspecified	0ft 0in
Hips + ridges	25ft 11in
Eaves + rakes	110ft 6in

Pitch 6/12

Area (sqft)	760
Squares	7.6

Recommended


Waste %	0%	10%	12%	15%	17%	20%	22%
Area (sqft)	760	836	851	874	889	912	927
Squares	7.6	8.4	8.6	8.8	8.9	9.2	9.3

Recommended waste is based on an asphalt shingle roof with a closed valley system (if applicable). Several other factors are involved in determining which waste percentage to use, including the complexity of the roof and individual roof application style. You will also need to calculate the post-waste quantity of other materials needed (hip and ridge caps, starter shingle, etc.).

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Report summary

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

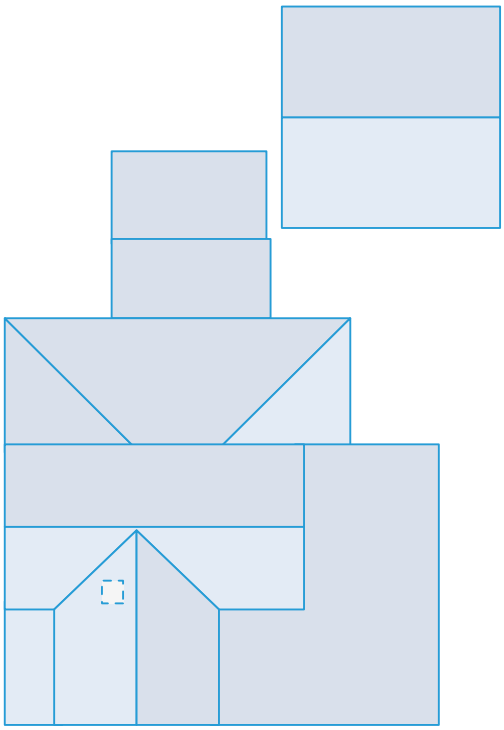

Measurements

Total roof area	3879 sqft
Total pitched area	3677 sqft
Total flat area	202 sqft
Total roof facets	13 facets
Predominant pitch	6/12
Total eaves	269ft 8in
Total valleys	30ft 0in
Total hips	47ft 11in
Total ridges	87ft 6in
Total rakes	226ft 3in
Total wall flashing	77ft 6in
Total step flashing	56ft 8in
Total transitions	18ft 10in
Total parapet wall	0ft 0in
Total unspecified	0ft 0in
Hips + ridges	135ft 5in
Eaves + rakes	495ft 11in

Pitch	1/12	3/12	4/12	6/12	8/12
Area (sqft)	203	183	858	1,489	1,149
Squares	2.1	1.9	8.6	14.9	11.5

Recommended

Waste %	0%	10%	12%	15%	17%	20%	22%
Area (sqft)	3,880	4,268	4,345	4,462	4,539	4,656	4,733
Squares	38.8	42.7	43.5	44.7	45.4	46.6	47.4

Recommended waste is based on an asphalt shingle roof with a closed valley system (if applicable). Several other factors are involved in determining which waste percentage to use, including the complexity of the roof and individual roof application style. You will also need to calculate the post-waste quantity of other materials needed (hip and ridge caps, starter shingle, etc.).

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.

Material calculations

9320 North Lost Creek-Shelby Road, Fletcher, OH 45326

Product	Unit	Waste (0%)	Waste (10%)	Waste (12%)	Waste (15%)
Shingle (total sqft)		3,678 sqft	4,045 sqft	4,119 sqft	4,229 sqft
IKO - Cambridge	bundle	111	122	124	127
CertainTeed - Landmark	bundle	113	124	126	129
GAF - Timberline	bundle	113	124	126	129
Owens Corning - Duration	bundle	113	124	126	129
Atlas - Pristine	bundle	112	123	125	129
Starter (eaves + rakes)		496 ft	546 ft	556 ft	571 ft
IKO - Leading Edge Plus	bundle	5	5	5	5
CertainTeed - SwiftStart	bundle	5	5	5	5
GAF - Pro-Start	bundle	5	5	5	5
Owens Corning - Starter Strip	bundle	5	6	6	6
Atlas - Pro-Cut	bundle	4	4	4	5
Ice and Water (eaves + valleys + flashings)		434 ft	478 ft	486 ft	499 ft
IKO - StormShield	roll	7	8	8	8
CertainTeed - WinterGuard	roll	7	8	8	8
GAF - WeatherWatch	roll	7	8	8	8
Owens Corning - WeatherLock	roll	6	7	7	7
Atlas - Weathermaster	roll	7	8	8	8
Synthetic (total sqft; no laps)		3,678 sqft	4,045 sqft	4,119 sqft	4,229 sqft
IKO - Stormtite	roll	4	5	5	5
CertainTeed - RoofRunner	roll	4	5	5	5
GAF - Deck-Armor	roll	4	5	5	5
Owens Corning - RhinoRoof	roll	4	5	5	5
Atlas - Summit	roll	4	5	5	5
Capping (hips + ridges)		136 ft	149 ft	152 ft	156 ft
IKO - Hip and Ridge	bundle	4	4	4	4
CertainTeed - Shadow Ridge	bundle	5	5	6	6
GAF - Seal-A-Ridge	bundle	6	6	7	7
Owens Corning - DecoRidge	bundle	7	8	8	8
Atlas - Pro-Cut H&R	bundle	5	5	5	6
Other					
8' Valley (no laps)	sheet	4	5	5	5
10' Drip Edge (eaves + rakes; no laps)	sheet	50	55	56	58

These calculations are estimates and are not guaranteed. Always double check calculations before ordering materials. Estimates are based off of the total pitched area (i.e., flat area is excluded).

This report was powered by Roofr. Copyright © 2026 Roofr.com | All rights reserved.
